




Rail Baltica Forum

Brussels, March 5, 2020

Work progress on Rail Baltica in Poland


Works on the E75 railway line Warszawa – Trakiszki (state border)

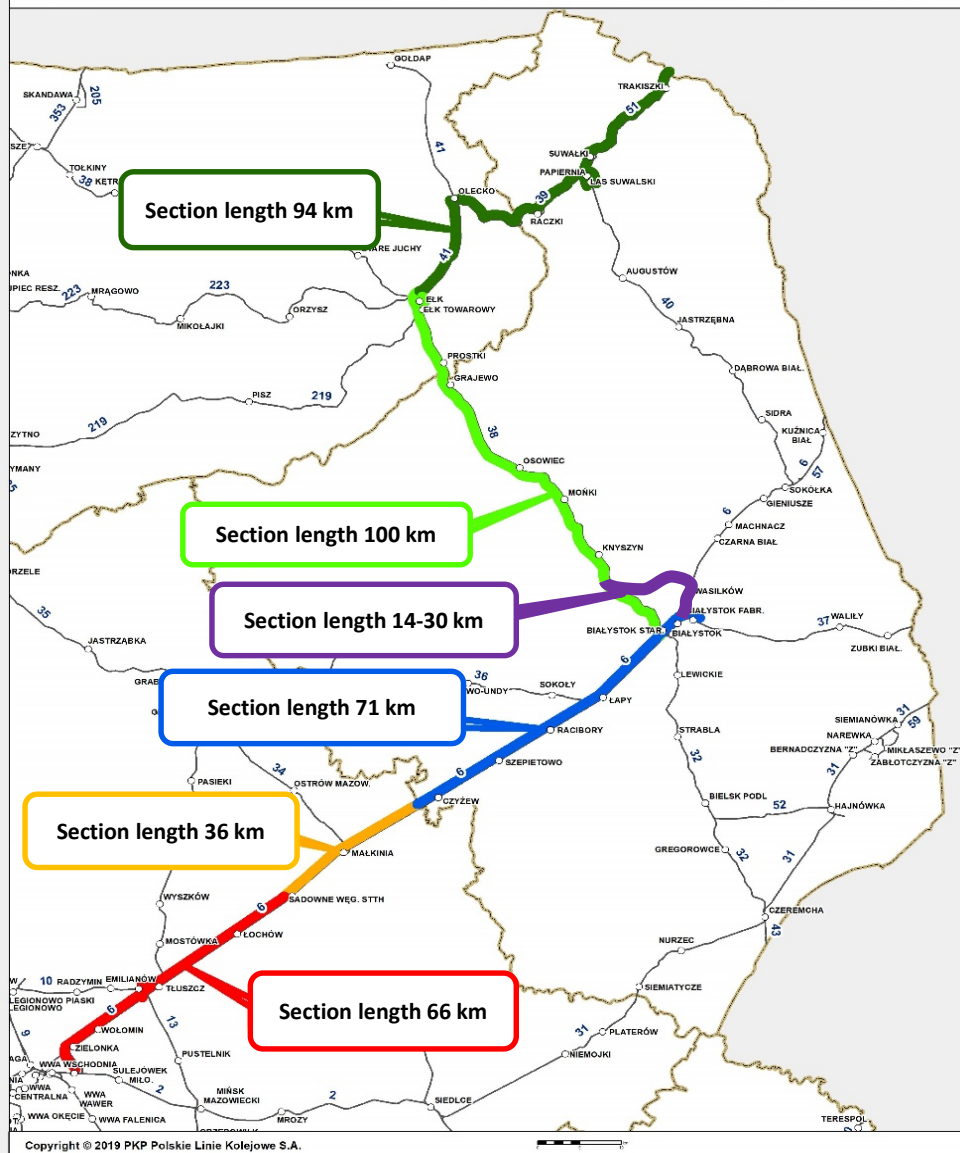

Status	Section	Section length [km]
Project completed	Warszawa– Tłuszcz (Sadowne)	66
Construction works were completed in the scope of putting into service tracks no. 1 and 2	Sadowne – Czyżew	36
Before signing the contract for construction works	Czyżew – Białystok	71
Study documentation is being prepared	Białystok North Bypass	14 – 30 (depending on variant chosen)
Designing and obtaining building permit decisions in progress	Białystok – Elk	100
Study documentation is being prepared	Elk - Trakiszki	94
Rail Baltica in Poland		381 - 397

Implementation of works on Rail Baltica, in Poland in the years 2020-2027

Works on the E75 railway line Warszawa – Trakiszki (state border)

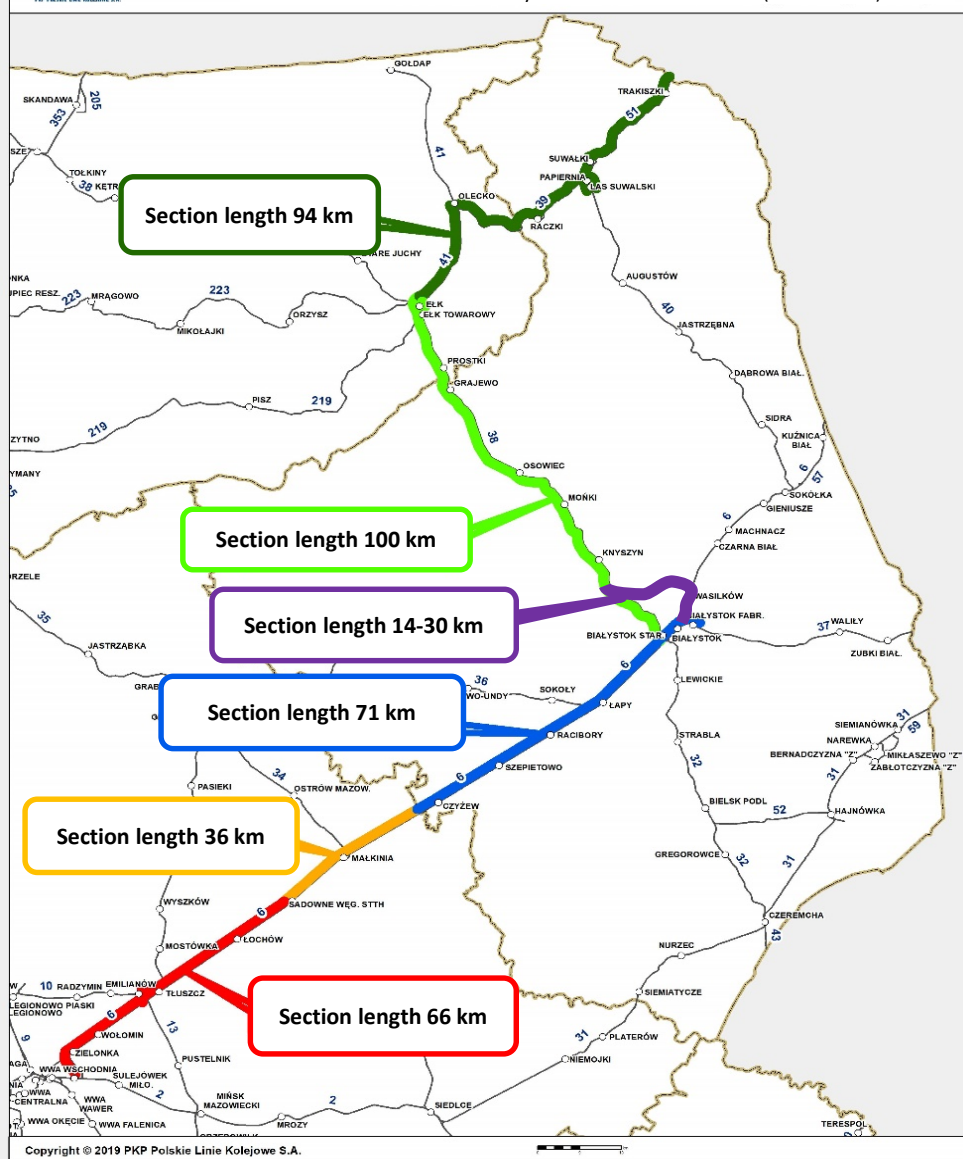

Status	Section
<ol style="list-style-type: none"> 1. Construction traction substations 110kV in: Dobczyn, Szewnica, Sadowne Węgrowskie - planned date for completion of construction: 4Q2021. 	Warszawa–Tłuszcz (Sadowne)
<ol style="list-style-type: none"> 1. Preparation of project documentation for 7 intersections. 2. Completion of works – 1 Q 2022. 	Sadowne – Czyżew
<ol style="list-style-type: none"> 1. Signing the contract for construction works - 2Q 2020. 2. Implementation of works planned - 2020-2023. 	Czyżew – Białystok
<ol style="list-style-type: none"> 1. Completion of the documentation study - 2Q 2021. 2. Preparation of project documentation along with obtaining all administrative decisions - 2021-2024 3. The implementation of construction works is planned for 2024-2027. 	Białystok North Bypass
<ol style="list-style-type: none"> 1. Planned completion of documentation - 3Q 2021. 2. Announcement of a tender for works for the Elk station – 4Q 2020. 3. Implementation of works at the Elk station – 2021-2023. 4. Implementation of the remaining works on the Białystok - Elk section together with ETCS - 2022-2025. 	Białystok – Elk
<ol style="list-style-type: none"> 1. Study documentation is being prepared - planned completion of the variants analysis - 2Q 2020. 2. Announcement of the tender for project documentation - 2Q 2020. 3. Completion of the documentation stage - 2023. 4. Announcement of a tender for works - 2023. 5. Implementation of construction works including ETCS - 2023-2027. 	Elk - Trakiszki



PKP POLSKIE LINIE KOLEJOWE S.A.

Zarządca narodowej sieci linii kolejowych



Thank you for your attention

